


Muenster PubWorks Update July 4, 2024.

Weather pending!

Public Works Completed to Date July 3, 2024:
\$90,000.00 for Contractor equip/ labour, gravel and culverts referenced within in green road sections including Taphorn, Phillips, Main .

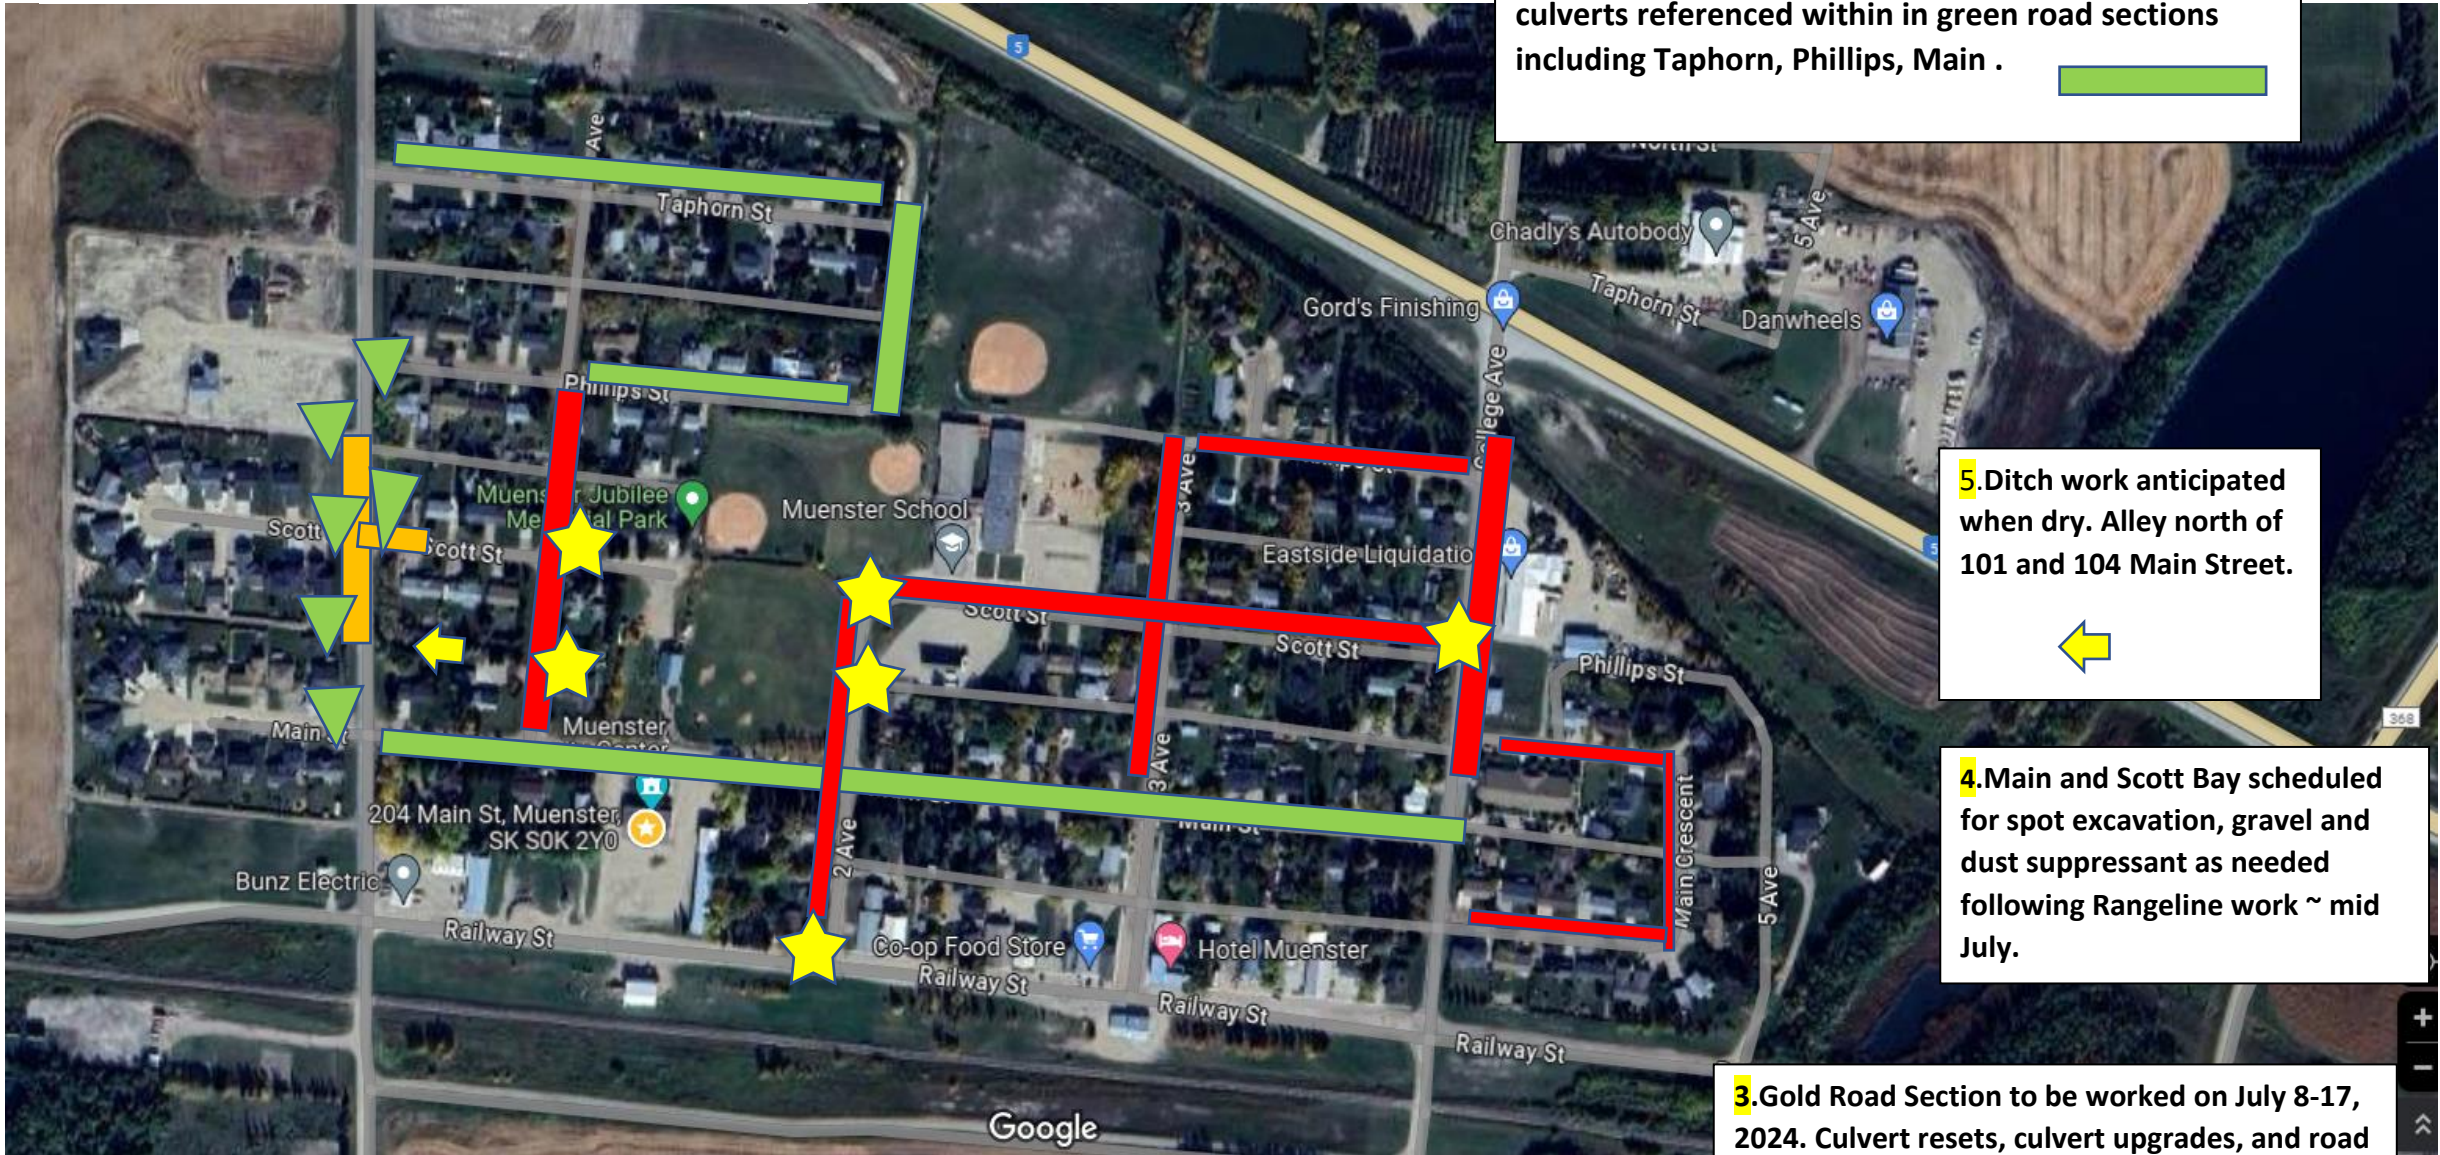

5. Ditch work anticipated when dry. Alley north of 101 and 104 Main Street.

4. Main and Scott Bay scheduled for spot excavation, gravel and dust suppressant as needed following Rangeline work ~ mid July.

3. Gold Road Section to be worked on July 8-17, 2024. Culvert resets, culvert upgrades, and road building. Green triangle show culverts focused on.

1. Green road Sections complete - July 3, 2024. Shaping, base gravel and top gravel. Yellow Stars show Culverts improved/replaced.

2. Red Section actively worked on July 4-5 and 8-10th, 2024. Top gravel being added. Expect to see: gravel dumps, grader work, packing then dust suppressant – avoid parking on streets if you can.
